

ALMONDBANK FLOOD PROTECTION SCHEME – PHASE 1 PROGRESS PHOTOGRAPHS

December 2014 - Scheme commences!



Early January 2015 – Preparatory and demolition works continue at Bowling Club



Late January 2015 – Excavation completed for flood wall foundations and the unfortunate Service Utility issue that resulted in the roots of the mature tree being cut (the tree is due to be felled shortly).



February 2015 - Erection of flood wall reinforcement; pouring of concrete structure; and installation of carrier drain in football pitch (to take surface water from Main Street to River Almond).




March 2015 – Demolition of Pavilion.



April 2015 – Facing brick being constructed around flood wall



May 2015 – Construction of Main Street road drainage and continuation of flood wall construction around the Bowling Club. Mature tree felled.

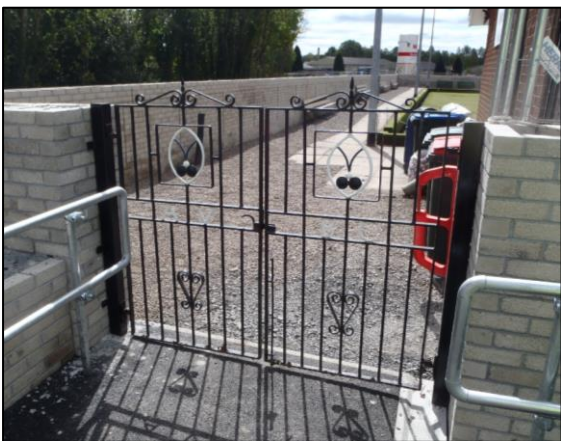



**July 2015 – Completion of Main Street road drainage and Bowling Club flood wall.
Installation of netting to prevent birds nesting prior to embankment protection works
(rock armour).**



September 2015 – Ongoing rock armour protection works to embankment adjacent to former pavilion.



October 2015 – Ongoing rock armour protection works - upstream section complete. Reinforced concrete gas main protection system being constructed.



November 2015 – Ongoing rock armour embankment protection works. Gas main protection system complete. High flow event delays works.



December 2015 – River Almond high flow event reaches underside of Black Bridge (to be replaced and raised as part of Contract 2) and flood water spills onto football/cricket pitch (this will be a flood storage area as part of Contract 2).



February 2015 – Rock Armour protection works complete. Contract 1 substantially complete.

